

*Hicksville Union Free School District
July 2019 Construction Report*



HICKSVILLE
Public Schools



PARK EAST CONSTRUCTION

Prepared by Ryan Badke

Table of Contents

- ▶ **Section I - Work Progress Through the Month July 2019**
- ▶ **Section II - Projected Work Through the Month of August 2019**
- ▶ **Section III – Progress Photos**
- ▶ **Section IV - Manpower Graph**



Work Completed Throughout the Month of July

- ▶ **Hicksville High School (Third Floor)**
 - ▶ Mounted 26 new Unit Ventilators (UV) on the third floor.
 - ▶ Completed connection of power wires, control wiring, refrigerant piping and condensate lines to 19 UVs in the east wing of the third floor.
 - ▶ All piping and wiring for these 19 units has been roughed up to the roof and pitch pockets have been installed to ensure the penetrations are weatherproof.
 - ▶ Completed installation and wiring for control devices connected to the fin tube assembly.
 - ▶ Began installation of refrigerant piping and condensate lines in the second wing of the third floor.



Work Completed Throughout the Month of July

- ▶ **Hicksville High School (Auditorium)**
 - ▶ Completed non abatement demolition in the auditorium
 - ▶ Established containment and began abatement of the ceiling plaster in the auditorium.
 - ▶ Completed the demolition of existing air handling equipment in fan room 1 adjacent to the auditorium.
 - ▶ Began the demolition of existing air handling equipment in fan room 2.
 - ▶ Cut 6 roof penetrations over tech rooms to allow access to install steel dunnage to support the two new roof top air handling units.
 - ▶ Completed all demolition in the kitchen, cafeteria A and cafeteria B.



Work Completed Throughout the Month of July

- ▶ **Hicksville High School (Kitchen and Cafeteria)**
 - ▶ Completed all demolition in the kitchen, cafeteria A and cafeteria B.
 - ▶ Completed the abatement of wall plaster in the cafeteria kitchen.
 - ▶ Completed framing of the new walls in cafeteria A, cafeteria B and the kitchen.
 - ▶ Began installing new power and data outlets in the cafeterias.
 - ▶ Completed lighting fixture conduit installation in both cafeterias.
 - ▶ Cut in three new door openings for hallway and kitchen access.
 - ▶ Began masonry infills of existing openings.
 - ▶ Installed new door frames and lintels.
 - ▶ Began plumbing rough ins for the new kitchen equipment.
 - ▶ Began installation of new gas piping for roof top air handling units.



Work Completed Throughout the Month of July

▶ Hicksville Middle School

- ▶ Completed abatement and demolition in the existing nurse's office.
- ▶ Completed demolition in the existing vestibule.
- ▶ Began framing and installing drywall in the new nurse's office and security vestibule.
- ▶ Completed installation of conduits running from the new service room to new sub panels on the second and third floor.
- ▶ Removed existing UVs on the third and second floor.



Work Completed Throughout the Month of July

- ▶ Burns Avenue Elementary
 - ▶ Completed demolition and abatement in the library.
 - ▶ Completed framing of new walls in the library.
 - ▶ Cut in new door ways into the library.
 - ▶ Existing openings have been infilled with CMU.
 - ▶ Existing casework removed in rooms 140-145.
 - ▶ Existing UVs removed in rooms 140-145.
 - ▶ Completed plumbing rough ins for the new library.



Work Completed Throughout the Month of July

- ▶ Dutch Lane Elementary
 - ▶ Existing casework removed in rooms 140-145.
 - ▶ Existing UVs removed in rooms 140-145.
 - ▶ Water main and hot water heater have been relocated.
 - ▶ Began demolition of three classrooms scheduled to become the new library and computer room.
 - ▶ Refrigerant piping for new UVs has been roughed up to the roof in six classrooms.
 - ▶ Control wiring has been roughed in to new UV locations and thermostats in six classrooms.
 - ▶ New casework has been assembled in six class rooms.



Work Completed Throughout the Month of July

▶ East Street Elementary

- ▶ Began abatement in room 105 storage closet.
- ▶ Installed new ceiling cassette air conditioner in the security office.
- ▶ Completed demolition in the existing band room, main office and principal's office.
- ▶ New flooring installed in the existing main office and principal's office which are scheduled to become new classrooms.
- ▶ Water main has been relocated in preparation for new electrical equipment.
- ▶ New 4" door frame has been installed in the current electrical room to allow for new equipment to be installed.
- ▶ Began installation of new condensers.
- ▶ Curbs for rooftop condensers have been set.
- ▶ Completed directional boring for new electrical service.



Work Completed Throughout the Month of July

▶ Fork Lane Elementary

- ▶ Existing casework removed in rooms 139-142, 144 and 145.
- ▶ Existing UVs removed in rooms 139-142, 144 and 145.
- ▶ Completed abatement in rooms 146 and 147
- ▶ Completed directional boring for new electrical service.
- ▶ Completed infilling existing openings into the library
- ▶ Completed framing of new walls in the library.
- ▶ Began roughing in new electrical outlets and fixtures.
- ▶ Completed installation of permanent wiring for lighting fixtures than reinstalled temporary lighting in all locations in the library.
- ▶ Completed installation of new electrical panel in the hallway outside of the library.
- ▶ Began pulling feed wires to new panels located outside of the library.
- ▶ Roughed in refrigerant piping for new UVs.
- ▶ Roughed in electrical feeds for new UVs in six classrooms.
- ▶ Completed plumbing rough ins for the new library.



Work Completed Throughout the Month of July

- ▶ **Lee Avenue Elementary**
 - ▶ Curbs for rooftop condensers have been set.
 - ▶ No other work until summer programs end.
- ▶ **Woodland Elementary**
 - ▶ No work until summer programs end.



Work Completed Throughout the Month of July

▶ Old Country Road Elementary

- ▶ Completed the abatement of floor tiles and cork board mastic in the library, room 140 and 141.
- ▶ Existing casework removed in rooms 144 and 146-151.
- ▶ Existing UVs removed in rooms 144 and 146-151.
- ▶ Completed demolition in the existing library.
- ▶ Completed framing in the library.
- ▶ Began roughing in new electrical outlets and fixtures.
- ▶ Completed installation of permanent wiring for lighting fixtures than reinstalled temporary lighting in all locations in the library.
- ▶ Completed installation of new electrical panel in the hallway outside of the library.
- ▶ Began pulling feed wires to new panels located outside of the library.
- ▶ Completed roughing in refrigerant piping in six classrooms and in the library.



Work Planned for the Month of August 2019

▶ Hicksville High School

- ▶ Complete abatement in the auditorium.
- ▶ Begin new construction in the auditorium.
- ▶ Complete the installation of all UVs on the third floor and all associated piping/wiring.
- ▶ Complete roofing replacement above the cafeteria and kitchen.
- ▶ Complete installation of new floors in the cafeteria.
- ▶ Complete installation of new electrical equipment in the cafeteria.
- ▶ Complete installation of new HVAC equipment in the cafeteria.
- ▶ Complete installation of new plumbing equipment in the cafeteria.
- ▶ Complete installation of new kitchen equipment in the cafeteria.
- ▶ Complete finish work in the new cafeteria.
- ▶ Perform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

▶ Hicksville Middle School

- ▶ Complete the installation of all UVs on the third floor and all associated piping/wiring.
- ▶ Complete installation of new electrical equipment in the new nurse's office and security vestibule.
- ▶ Complete installation of new subpanels.
- ▶ Complete installation of new plumbing equipment in the new nurse's office.
- ▶ Complete installation of new HVAC equipment in the new nurse's office.
- ▶ Complete finish work in the new nurse's office and security vestibule.
- ▶ Perform electrical shutdown and installation of new switchgear.
- ▶ Complete installation of new ceiling grid and tiles in all corridors.



Work Planned for the Month of August 2019

- ▶ **Burns Avenue Elementary**
 - ▶ Complete installation of new electrical equipment in the library.
 - ▶ Complete installation of new HVAC equipment in the library.
 - ▶ Complete installation of new plumbing equipment in the library.
 - ▶ Complete finish work and installation of new casework in the library and six classrooms.
 - ▶ Preform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

- ▶ Dutch Lane Elementary
 - ▶ Complete installation of new electrical equipment in the library.
 - ▶ Complete installation of new HVAC equipment in the library.
 - ▶ Complete installation of new plumbing equipment in the library.
 - ▶ Complete finish work and installation of new casework in the library and six classrooms.
 - ▶ Perform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

▶ East Street Elementary

- ▶ Complete installation of new electrical equipment in the new main office and principal's office.
- ▶ Complete installation of new HVAC equipment in the new main office and principal's office.
- ▶ Complete installation of new plumbing equipment in the new main office and principal's office.
- ▶ Complete finish work and installation of new casework in new main office and principal's office.
- ▶ Complete installation of new electrical equipment in the new band room.
- ▶ Complete finish work and installation of new casework in the new band room.
- ▶ Complete finish work in the old principal's office and main office.
- ▶ Complete installation of six new UVs on the third floor.
- ▶ Perform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

- ▶ Fork Lane Elementary
 - ▶ Complete installation of new electrical equipment in the library.
 - ▶ Complete installation of new HVAC equipment in the library.
 - ▶ Complete installation of new plumbing equipment in the library.
 - ▶ Complete finish work and installation of new casework in the library and six classrooms.
 - ▶ Perform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

- ▶ Lee Avenue Elementary
 - ▶ Complete installation of new UVs, condensers and all associated piping.
 - ▶ Preform electrical shutdown and installation of new switchgear.
- ▶ Woodland Elementary
 - ▶ Complete installation of new UVs, condensers and all associated piping.
 - ▶ Preform electrical shutdown and installation of new switchgear.



Work Planned for the Month of August 2019

- ▶ Old Country Road Elementary
 - ▶ Complete installation of new electrical equipment in the library.
 - ▶ Complete installation of new HVAC equipment in the library.
 - ▶ Complete installation of new plumbing equipment in the library.
 - ▶ Complete finish work and installation of new casework in the library and six classrooms.




High School



New doorways cut with new frames and lintels installed.

High School

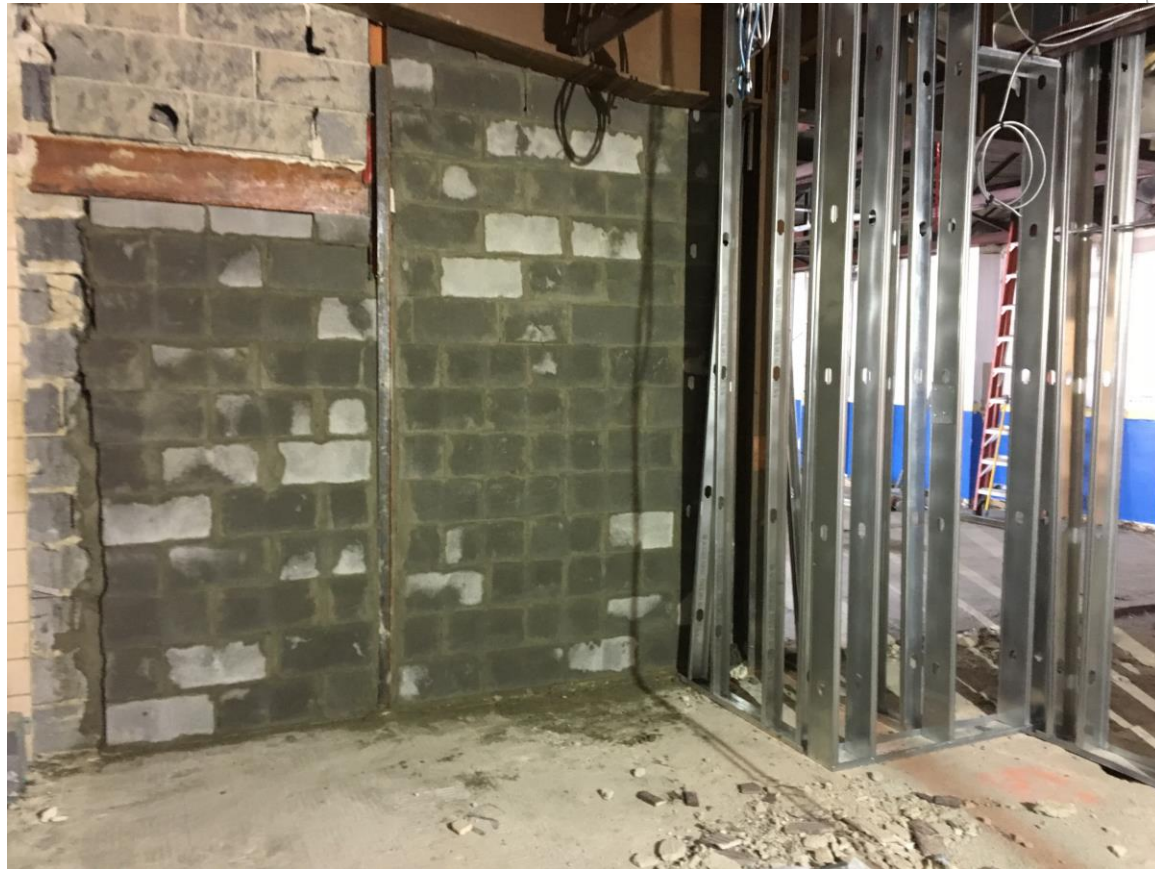

Existing openings in the cafeteria/kitchen have been infilled with CMU block.



High School



Completed framing and rough in of outlets and data ports
in the cafeteria.



High School



New shutoff valves and copper pipes feeding the kitchen have been installed in the basement and boiler room



High School



July 2019

Began welding 3" gas pipe sections together above the auxiliary gym.

High School



New control valves installed on existing fin tube lines.



High School



Completed demolition of fan room 1.



High School



Broke ground on new tennis court installation.



Hicksville Middle School



Began framing in the new nurse's office.



Hicksville Middle School



Began installation of new ceiling grid in the corridor on the second floor.




Hicksville Middle School



Began construction of the new security vestibule.



Middle School

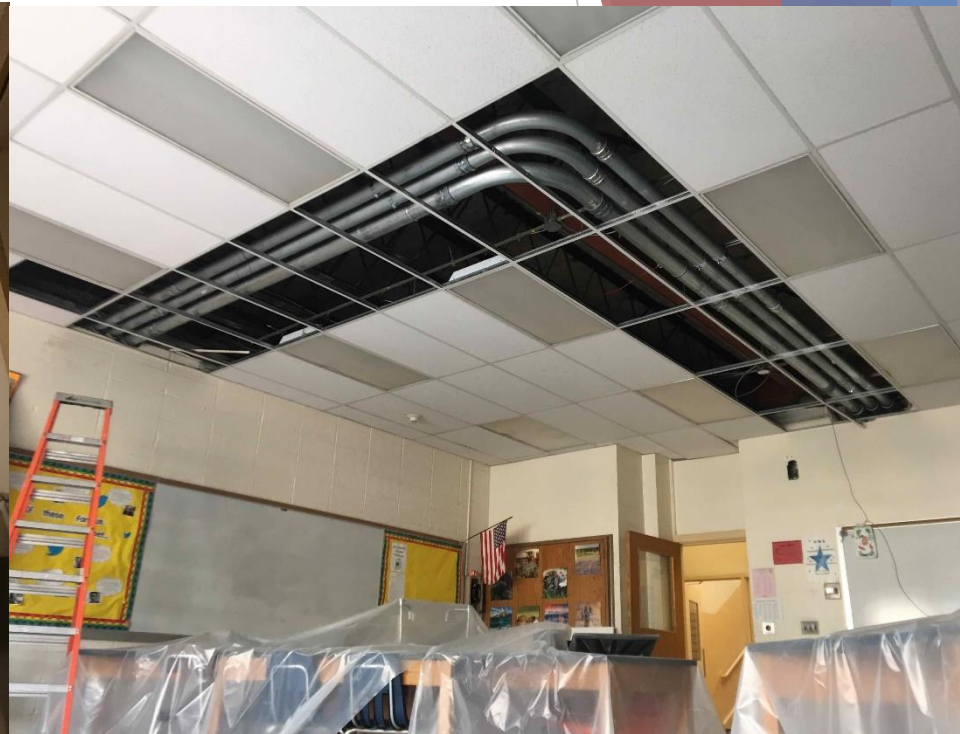

Splice box has been installed in the first-floor hallway. Pipe run continues in the ceiling of room 118 and up to the second-floor storage closet.



Burns and Old Country Road



Completed framing in the new libraries.



Dutch Lane and Old Country Road



New casework has been constructed and ready to be mounted to the wall.



Fork Lane and Old Country Road



Completed installation of new electrical panel outside of libraries.




East Street



New VCT flooring installed in the old principals office and main office.



East Street

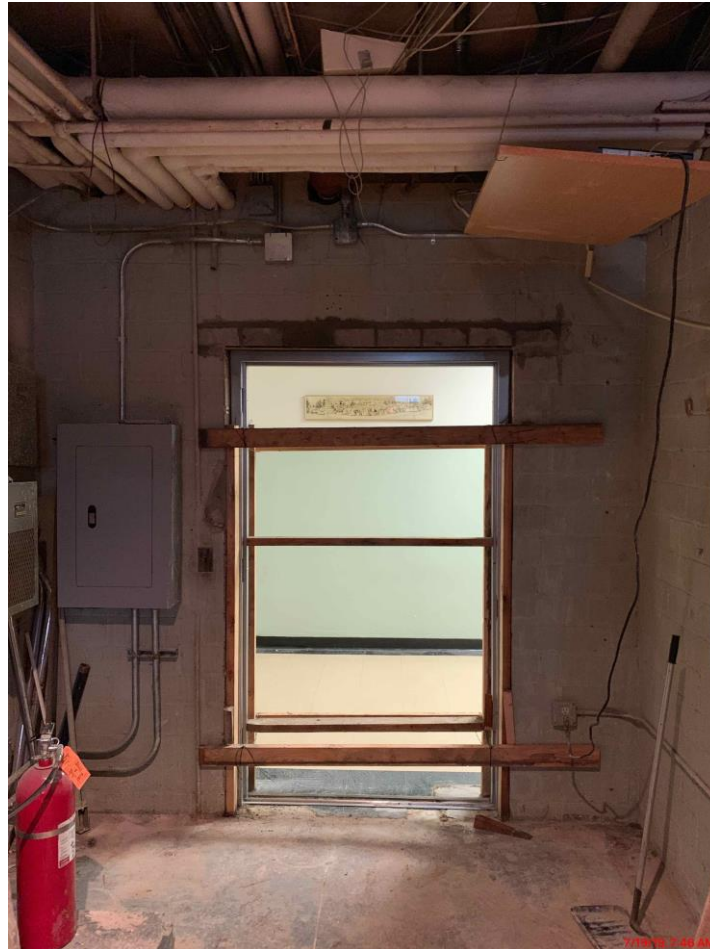

New 4' doorway installed in the meter room.

Dutch Lane



Relocated water main and hot water heater.

Hicksville Union Free School District Progress Report - Section IV

▼ MANPOWER GRAPH

